






Activity ID	Activity Name	Original Duration	Remaining Duration	Duration % Complete	Start	Finish
A3700	90% Plan Review By City	10	10	0%	20-Mar-17	31-Mar-17
A3040	CMAR Vendor Prequal & Selection Process	10	10	0%	24-Mar-17	06-Apr-17
A2700	Big Dig Plan Review	20	20	0%	20-Mar-17	14-Apr-17
A3050	CMAR CMP Estimate	15	15	0%	07-Apr-17	27-Apr-17
A3070	GMP Package to Commission Review/Approval	25	25	0%	28-Apr-17	01-Jun-17
Construction Documents (100% CD's)						
A2720	Meetings w/ City & CMAR	20	20	0%	03-Apr-17	28-Apr-17
A2730	Complete 100% Plans & Specs	20	20	0%	03-Apr-17	28-Apr-17
A2740	Plans to CMAR for final Bldg Dept Review	1	1	0%	01-May-17	01-May-17
NTP/DEMOLITION						
A3000	NTP Demo & Sitework	5	5	0%	25-May-17	31-May-17
A2000	Permitting	40	40	0%	02-May-17	26-Jun-17
A2010	NTP - Vertical Construction	1	1	0%	27-Jun-17	27-Jun-17
A2340	Early Release Demo & Sitework Permit	30	30	0%	01-Jun-17	13-Jul-17
A2040	Relocate Activity Center	1	1	0%	02-Jul-18	02-Jul-18
DEMOLITION						
A3090	Phase 1 - Demolition Structures (up to Pool)	33	33	0%	14-Jul-17	29-Aug-17
A3170	Tree Relocation Root Pruning	90	90	0%	30-Aug-17	08-Jan-18
SITING						
A3530	Install Temporary Fence for phase 1A	3	3	0%	01-Jun-17	05-Jun-17
A2020	KL Mobilization / Subcontract	20	20	0%	01-Jun-17	28-Jun-17
A3660	MOT Set up	5	5	0%	29-Jun-17	05-Jul-17
A3540	Demol/Grade Phase 1 Area	30	30	0%	07-Jul-17	17-Aug-17
A3010	Remove Existing Sanitary Main (Old Federal)	5	5	0%	11-Aug-17	17-Aug-17
A3890	Remove/Relocate Existing Communication Lines	60	60	0%	29-Jun-17	23-Sep-17
A4010	Remove Existing Water Main (Old Federal)	10	10	0%	18-Sep-17	29-Sep-17
A3690	FPL	45	45	0%	02-Oct-17	04-Dec-17
A4220	Storage Material Area	15	15	0%	15-Nov-17	06-Dec-17
A4210	Perimeter Fencing (partial)	20	20	0%	07-Dec-17	05-Jan-18
4th Avenue						
A3430	Clear and Grade SE 4th Avenue	5	5	0%	07-Jul-17	13-Jul-17
A2030	Install Sanitary Main SE 4th Avenue	10	10	0%	14-Jul-17	27-Jul-17
A3470	Install Storm Structures SE 4th Avenue	10	10	0%	28-Jul-17	10-Aug-17
A3920	Tie In 4th St Sanitary to Existing/Inspections	10	10	0%	28-Jul-17	10-Aug-17
A3440	Install Water Main SE 4th Avenue	5	5	0%	11-Aug-17	17-Aug-17
A3690	Testing/Inspection Water Main SE 4th Ave	20	20	0%	18-Aug-17	16-Sep-17
A3490	Subgrade/Curb/Liner/Asphalt SE 4th Avenue	20	20	0%	18-Sep-17	13-Oct-17
A3510	Asphalt SE 4th Avenue	5	5	0%	15-Oct-17	20-Oct-17
SE 7th Street						
A3450	Install Sanitary Main SE 7th Street	15	15	0%	29-Jul-17	17-Aug-17
A3480	Install Storm Structures SE 7th Street	10	10	0%	11-Aug-17	24-Aug-17
A3460	Install Water Main SE 7th Street	10	10	0%	25-Aug-17	06-Sep-17
A3940	Testing/Inspection Water Main SE 7th Street	20	20	0%	11-Sep-17	06-Oct-17
A3670	Remove Existing Utilities SE 7th Street	10	10	0%	09-Oct-17	20-Oct-17
A3500	Subgrade/Curb/Liner/Asphalt SE 7th Street	25	25	0%	23-Oct-17	27-Nov-17
A3520	Asphalt SE 7th Street 1st Lift	5	5	0%	28-Nov-17	04-Dec-17
SE 5th Street						
A3970	Install Storm Structures SE 5th Street	10	10	0%	29-Aug-17	09-Sep-17
A3860	Install Fire Hydrant	5	5	0%	11-Sep-17	18-Sep-17
A3890	Subgrade/Curb/Liner/Asphalt SE 5th Street	15	15	0%	16-Oct-17	03-Nov-17
A4000	Asphalt SE 5th Street	5	5	0%	06-Nov-17	10-Nov-17
Concession Stand/Restrooms						
A3550	Foundations	10	10	0%	18-Aug-17	31-Aug-17
A3850	MEP Rough SOG	10	10	0%	01-Sep-17	15-Sep-17
A3560	Exterior Walls	20	20	0%	18-Sep-17	13-Oct-17
A3900	Joist/Roofing	15	15	0%	16-Oct-17	03-Nov-17
A3570	Finishes	30	30	0%	06-Nov-17	18-Dec-17
A4070	Grading/Pavers	15	15	0%	19-Dec-17	10-Jan-18
A4110	Field Lighting/Switch Gear/Elec Final	45	45	0%	06-Nov-17	10-Jan-18
Soccer/Multi Purpose Field						
A4020	Grass	15	15	0%	26-Jul-17	10-Aug-17
A4030	Grading	15	15	0%	11-Aug-17	31-Aug-17
A4040	Site Lighting	10	10	0%	01-Sep-17	15-Sep-17
A4050	Artificial Field	60	60	0%	15-Sep-17	11-Dec-17
A4250	Excavate Trail (Perimeter of Field)	10	10	0%	12-Dec-17	26-Dec-17
A4240	Landscaping/ Irrigation	10	10	0%	27-Dec-17	10-Jan-18
H.S. Field						
A3700	Drainage	20	20	0%	18-Aug-17	15-Sep-17
A3730	Grading	15	15	0%	18-Sep-17	05-Oct-17
A3710	Lighting	10	10	0%	09-Oct-17	20-Oct-17
A3740	Fencing/Backstop	20	20	0%	09-Oct-17	03-Nov-17
A3720	Irrigation	5	5	0%	09-Nov-17	10-Nov-17
A3850	Topsoil/Sod	20	20	0%	23-Oct-17	17-Nov-17
A3750	Benchers/ Dugout	20	20	0%	06-Nov-17	04-Dec-17
A4060	Landscaping	5	5	0%	28-Nov-17	04-Dec-17
Youth Field						
A3580	Drainage	15	15	0%	18-Sep-17	05-Oct-17
A3610	Grading	10	10	0%	09-Oct-17	20-Oct-17
A3590	Lighting	10	10	0%	23-Oct-17	03-Nov-17
A3620	Fencing/Backstop	20	20	0%	09-Nov-17	04-Dec-17
A3600	Irrigation	5	5	0%	05-Dec-17	11-Dec-17
A3830	Topsoil/Sod	15	15	0%	20-Nov-17	11-Dec-17
A4090	Landscaping	5	5	0%	12-Dec-17	18-Dec-17
A3630	Benchers/Dugout	20	20	0%	28-Nov-17	26-Dec-17
Tee Ball Field						
A3640	Drainage	7	7	0%	23-Oct-17	31-Oct-17
A3670	Grading	10	10	0%	01-Nov-17	14-Nov-17
A3650	Lighting	10	10	0%	16-Nov-17	29-Nov-17
A3680	Fencing/Backstop	15	15	0%	05-Dec-17	28-Dec-17
A3640	Topsoil/Sod	10	10	0%	12-Dec-17	28-Dec-17
A3660	Irrigation	5	5	0%	27-Dec-17	03-Jan-18
A4080	Batting Cages	40	40	0%	15-Nov-17	12-Jan-18
A4100	Landscaping	5	5	0%	09-Jan-18	15-Jan-18
A3890	Benchers and Dugout	20	20	0%	15-Dec-17	17-Jan-18
Field Parking Lot						
		97	97	0%	18-Aug-17	06-Jan-18


2017												2018												2019				
Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May		
90% Plan Review By City	CMAR Vendor Prequal & Selection Process	Big Dig Plan Review	CMAR CMP Estimate	GMP Package to Commission Review/Approval	Meetings w/ City & CMAR	Complete 100% Plans & Specs	Plans to CMAR for final Bldg Dept Review																					

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

Peter Bluesten Park @ Hallandale Beach EH COPY
Preliminary Schedule

Run Date: 14-Mar-17
Data Date: 11-Jan-16
Page 2 of 3



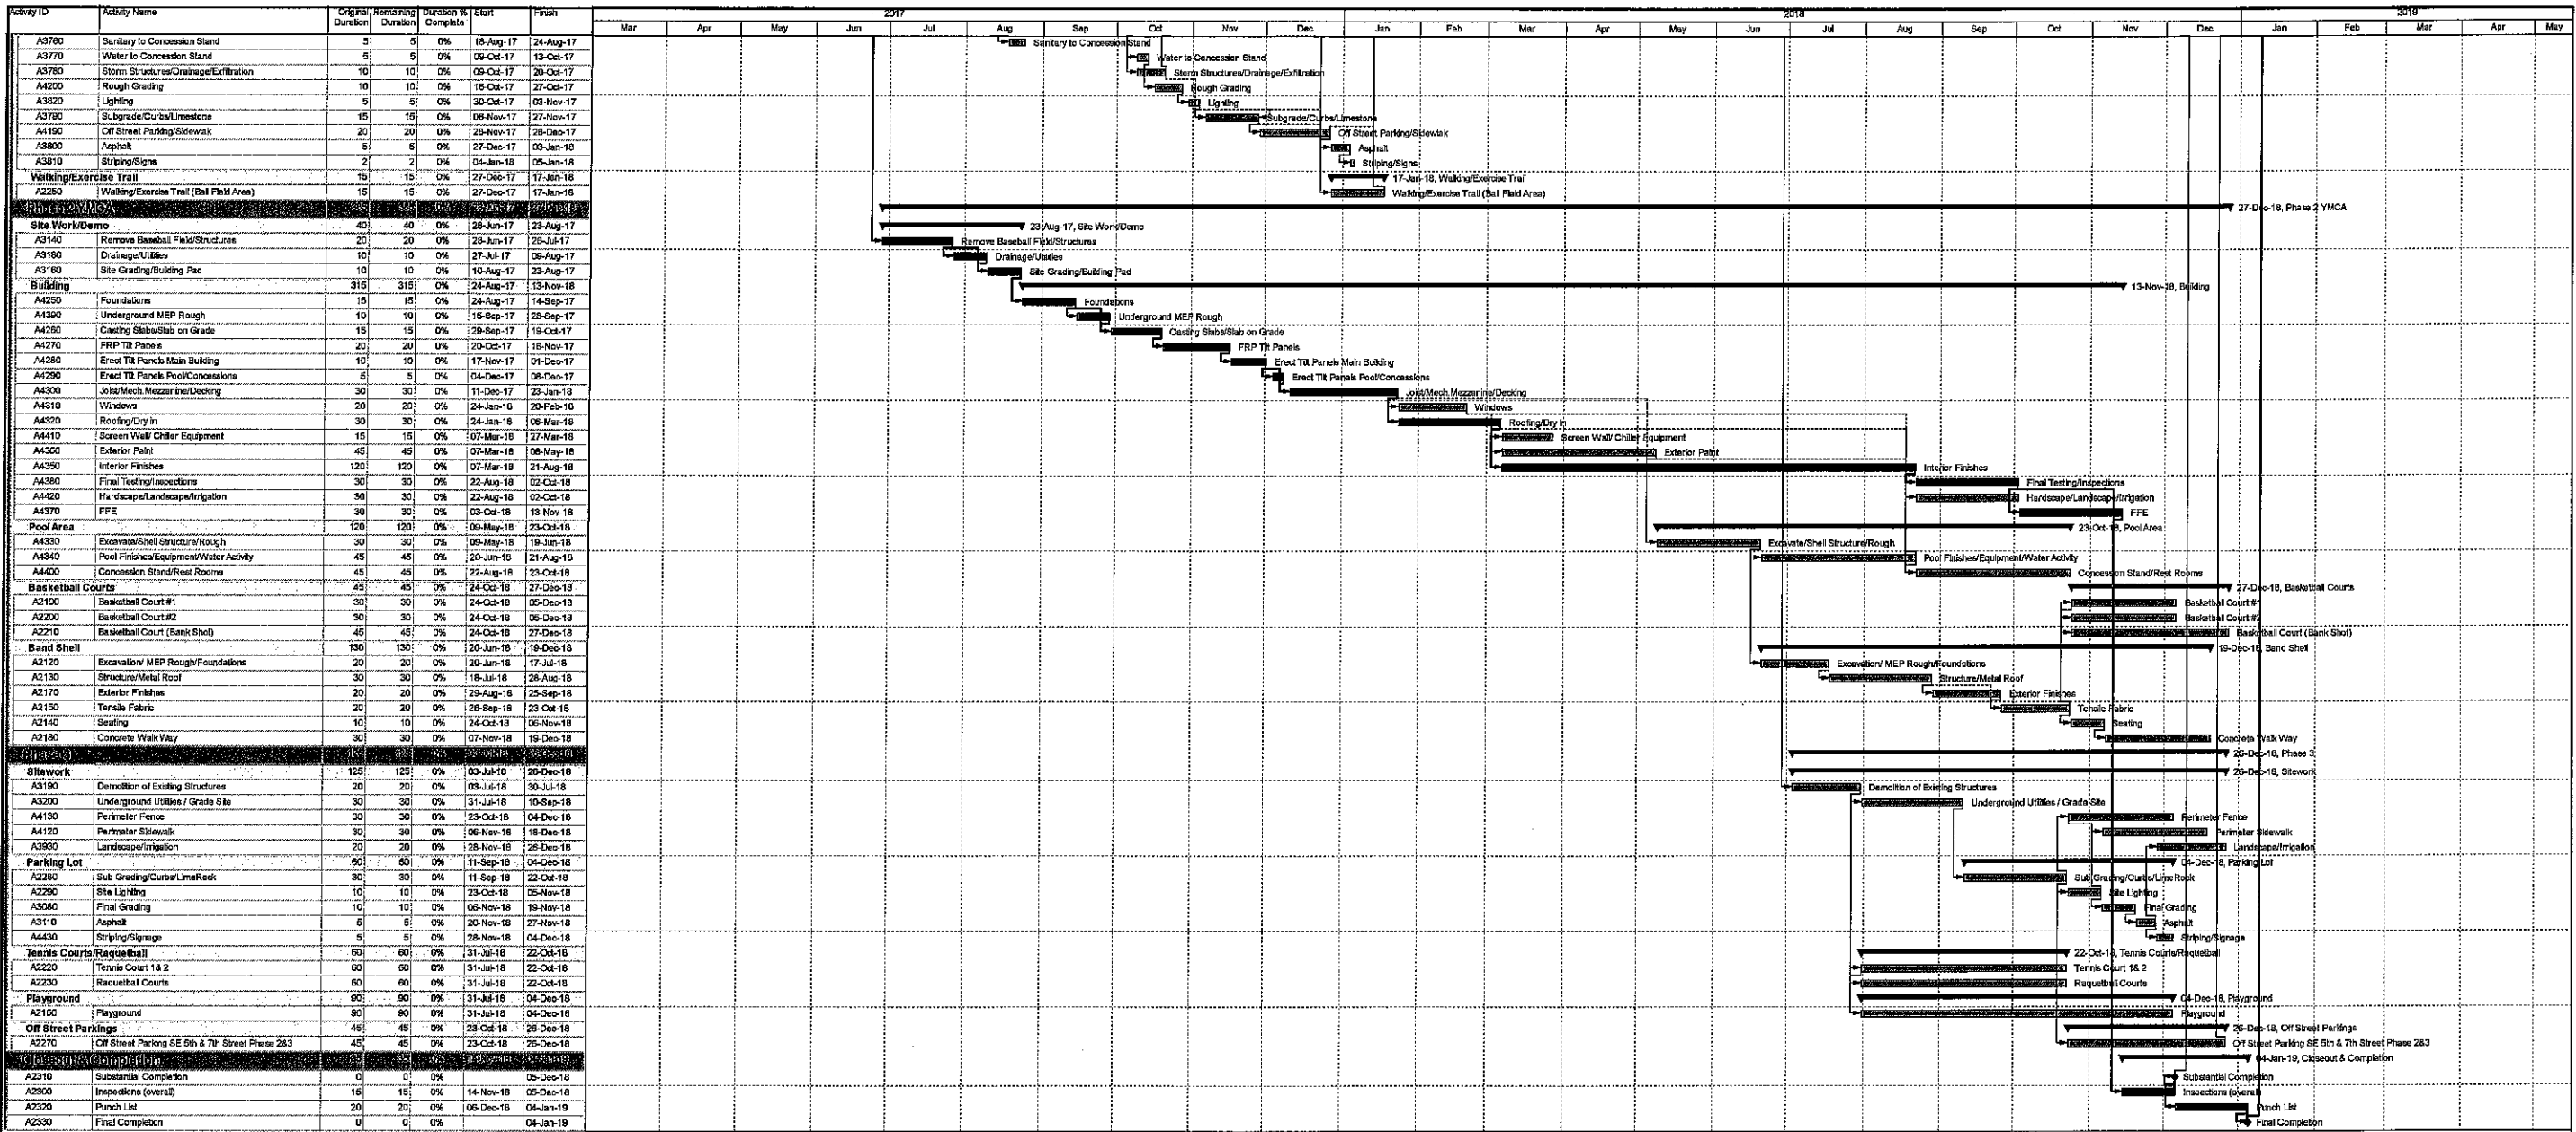

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

Peter Bluesten Park @ Hallandale Beach EH COPY
Preliminary Schedule

Run Date: 14-Mar-17
Data Date: 11-Jan-16
Page 3 of 3

