

CITY OF HALLANDALE BEACH, FLORIDA
MEMORANDUM


DATE: November 27, 2017
TO: Roger M. Carlton, City Manager
FROM: Steven F. Parkinson, P.E., PWLF, Assistant City Manager/Public Works Director
SUBJECT: A1A Bridge Painting Improvements – Project Status

The purpose of this memorandum is to provide a progress report to the City Manager for the A1A Bridge Painting Improvements Project.

1. **Project Scope:** painting of the bridge located at East Hallandale Beach Boulevard and Ocean Drive (A1A) to include: paint all bridge walls (currently depicted in coral/red color), under the bridge and columns (currently depicted as the original grey color of the concrete). The columns will be painted in blue (no rainbow).
2. **Exclusions:** the west face of the bridge manatee's artwork and steel component of the bridge depicted in yellow color on the Exhibit 1. The steel bridge is scheduled to be painted by FDOT in 2019. As per the meeting with the Florida Department of Transportation (FDOT) maintenance division and the City Engineer on October 9th, 2017, FDOT will use the color as per City preference.
3. **Project progress:**
Since the bridge belongs to FDOT, a Community Aesthetical Feature Agreement (CAFA) is required. CAFA requires the following steps:
 - Application submittal
 - Approval from FDOT
 - Provide a letter of credit, bond or check to FOT for an equal amount determined by the City to cover the cost in case that the City fails to provide the required maintenance. The City Engineer offered to FDOT a payment of \$15,000 and which they have agreed via an email.
 - A resolution adopted by the City Commission for the approval of the Agreement
 - Submit the Agreement executed by the City to the FDOT for their execution.

FDOT will inform the City when the payment shall be submitted (it is anticipated at any time after the approval, but prior the execution of the agreement between the City and FDOT).

Item Description	Date of Completion	Status
1st CAFA Requirements meeting with FDOT	August 31, 2017	Complete
2nd Coordination Meeting with FDOT	October 09, 2017	Complete
100% Conceptual Plans by ACAI (Exhibit B)	October 12, 2017	Complete
CAFA Permit Submitted to FDOT	October 26, 2017	Complete
Technical Specifications and Bid Documents provided in house by the engineering staff	December 31, 2017	In progress (80% completed)
Bid Package submittal to Procurement Department	TBD	Pending CAFA approval by FDOT
City Commission Resolution	TBD (maybe January or February, or even later)	Pending CAFA approval by FDOT
Bid Advertising	TBD	This can be done soon after CAFA approval, but it can be done before v City Commission approval of the resolution
Commencing painting	TBD	More accurate schedule can be provided after the CAFA approval

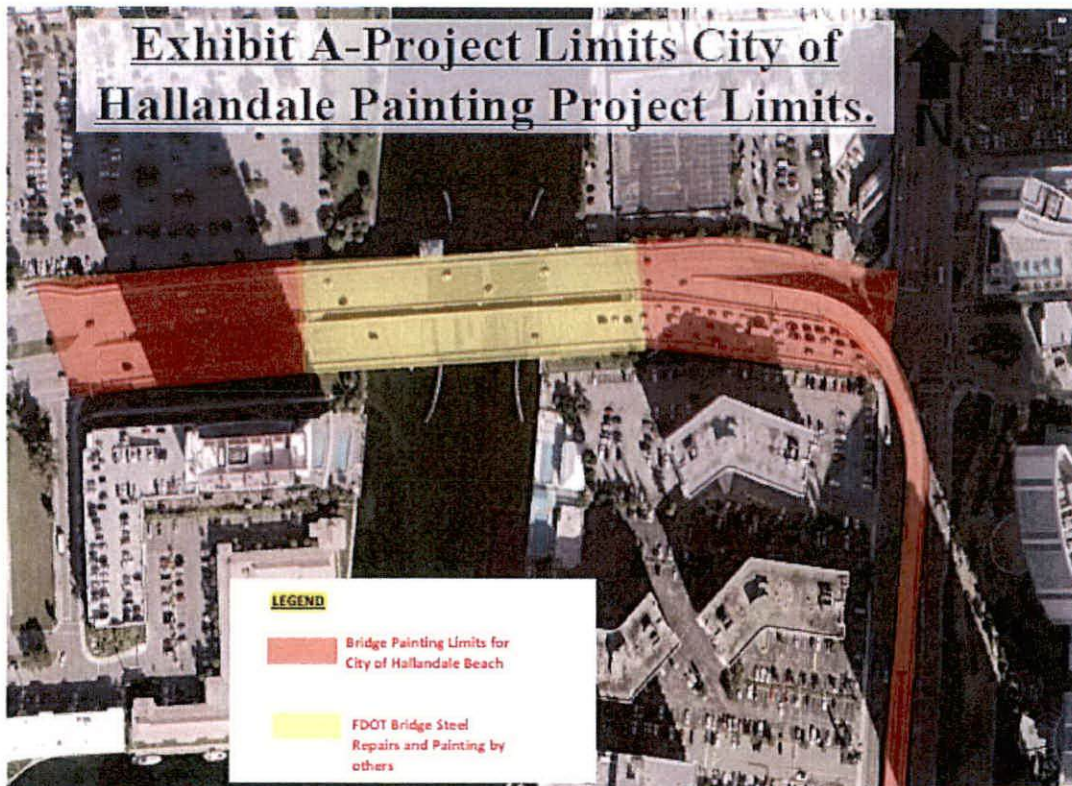

TO: Roger M. Carlton, City Manager
FROM: Steven Parkinson, Assistant City Manager / Public Works Director
RE: A1A Bridge Painting Project Status

Prepared By: Mariana Pitiriciu

Reviewed:



Roger M. Carlton, City Manager

11/30/17

Date



Approved

___ Denied

___ Hold for Discussion

Comments:
