



Update: Golden Isles Park & Tennis Center

Office of Capital Improvements

May 6, 2020

Update:

Golden Isles Tennis Center & Park



Original Timeline:

Start Construction	– 4 th Quarter of 2019
Complete Construction	– 4 th Quarter of 2020

Revised Timeline:

Construction Started	– 1 st Quarter of 2020
Substantial Completion Anticipated	– 1 st Quarter of 2021


(The project is currently 19% complete)

Cause of Delay: approval of Mangrove Protection Plan from Broward County -- entire west boundary of the park.

County permitting requirement resulted in shift of the entire Plan to the east



Golden Isles Tennis Center and Park

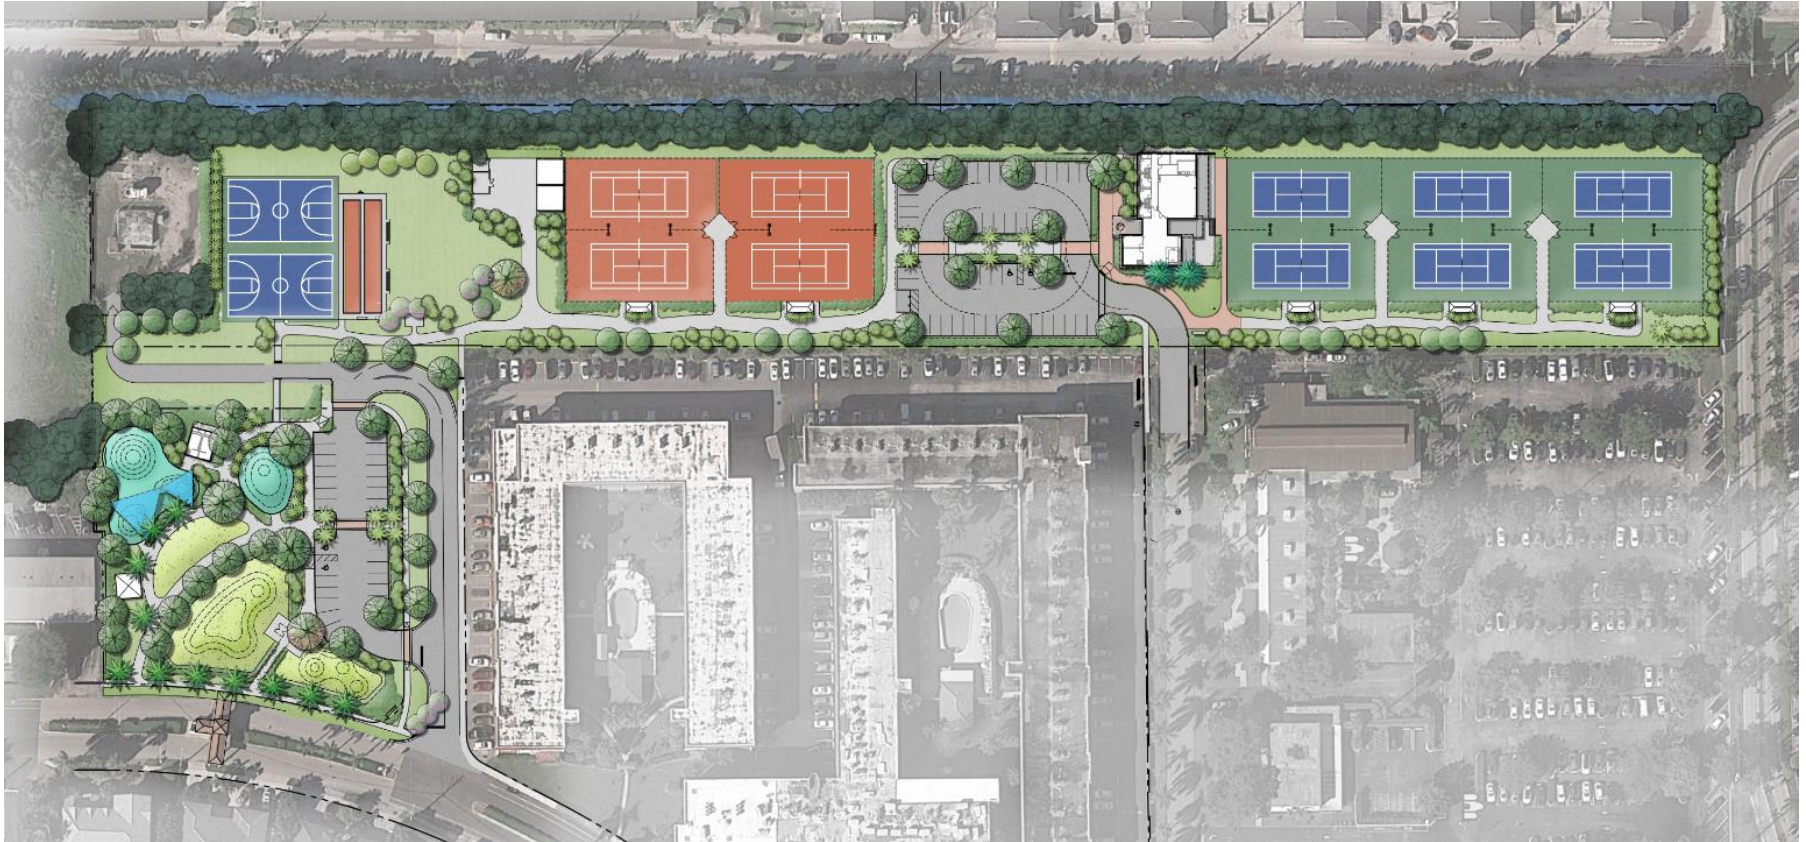

Golden Isles

Tennis Center and Park



The following major visible milestones can be expected:

- May through July - Mangrove trimming, drainage and underground work, building foundation construction, electrical infrastructure
- Mid-June – Visible vertical construction of Tennis Center.
- June/July - Tennis court construction
- September/October - Parking lot forming, restroom building vertical construction
- October/November – Sidewalks forming, roofing installation
- November/December – Landscaping and lighting
- January/February 2021 – Playground and furnishings
- February/March 2021 – Fencing



PROGRESS




BURKHARDT
CONSTRUCTION, INC.

Golden Isles Tennis Center & Park Improvements

SMITH
AERIAL
PHOTOS 03-23-20



PROGRESS

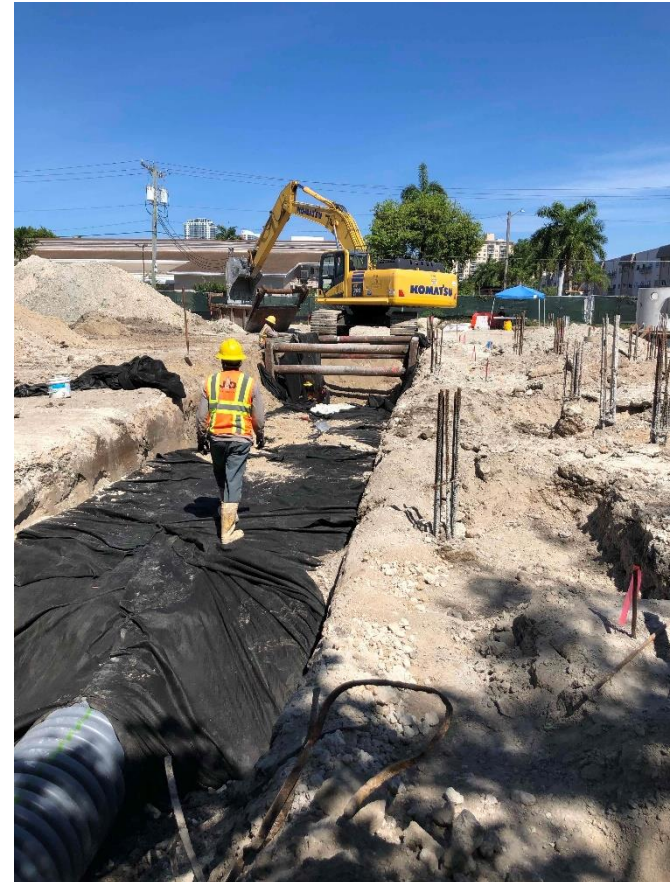

PROGRESS



PROGRESS



BURKHARDT
CONSTRUCTION, INC.

Golden Isles Tennis Center & Park Improvements

SMITH
AERIAL
PHOTOS 04-27-20

