


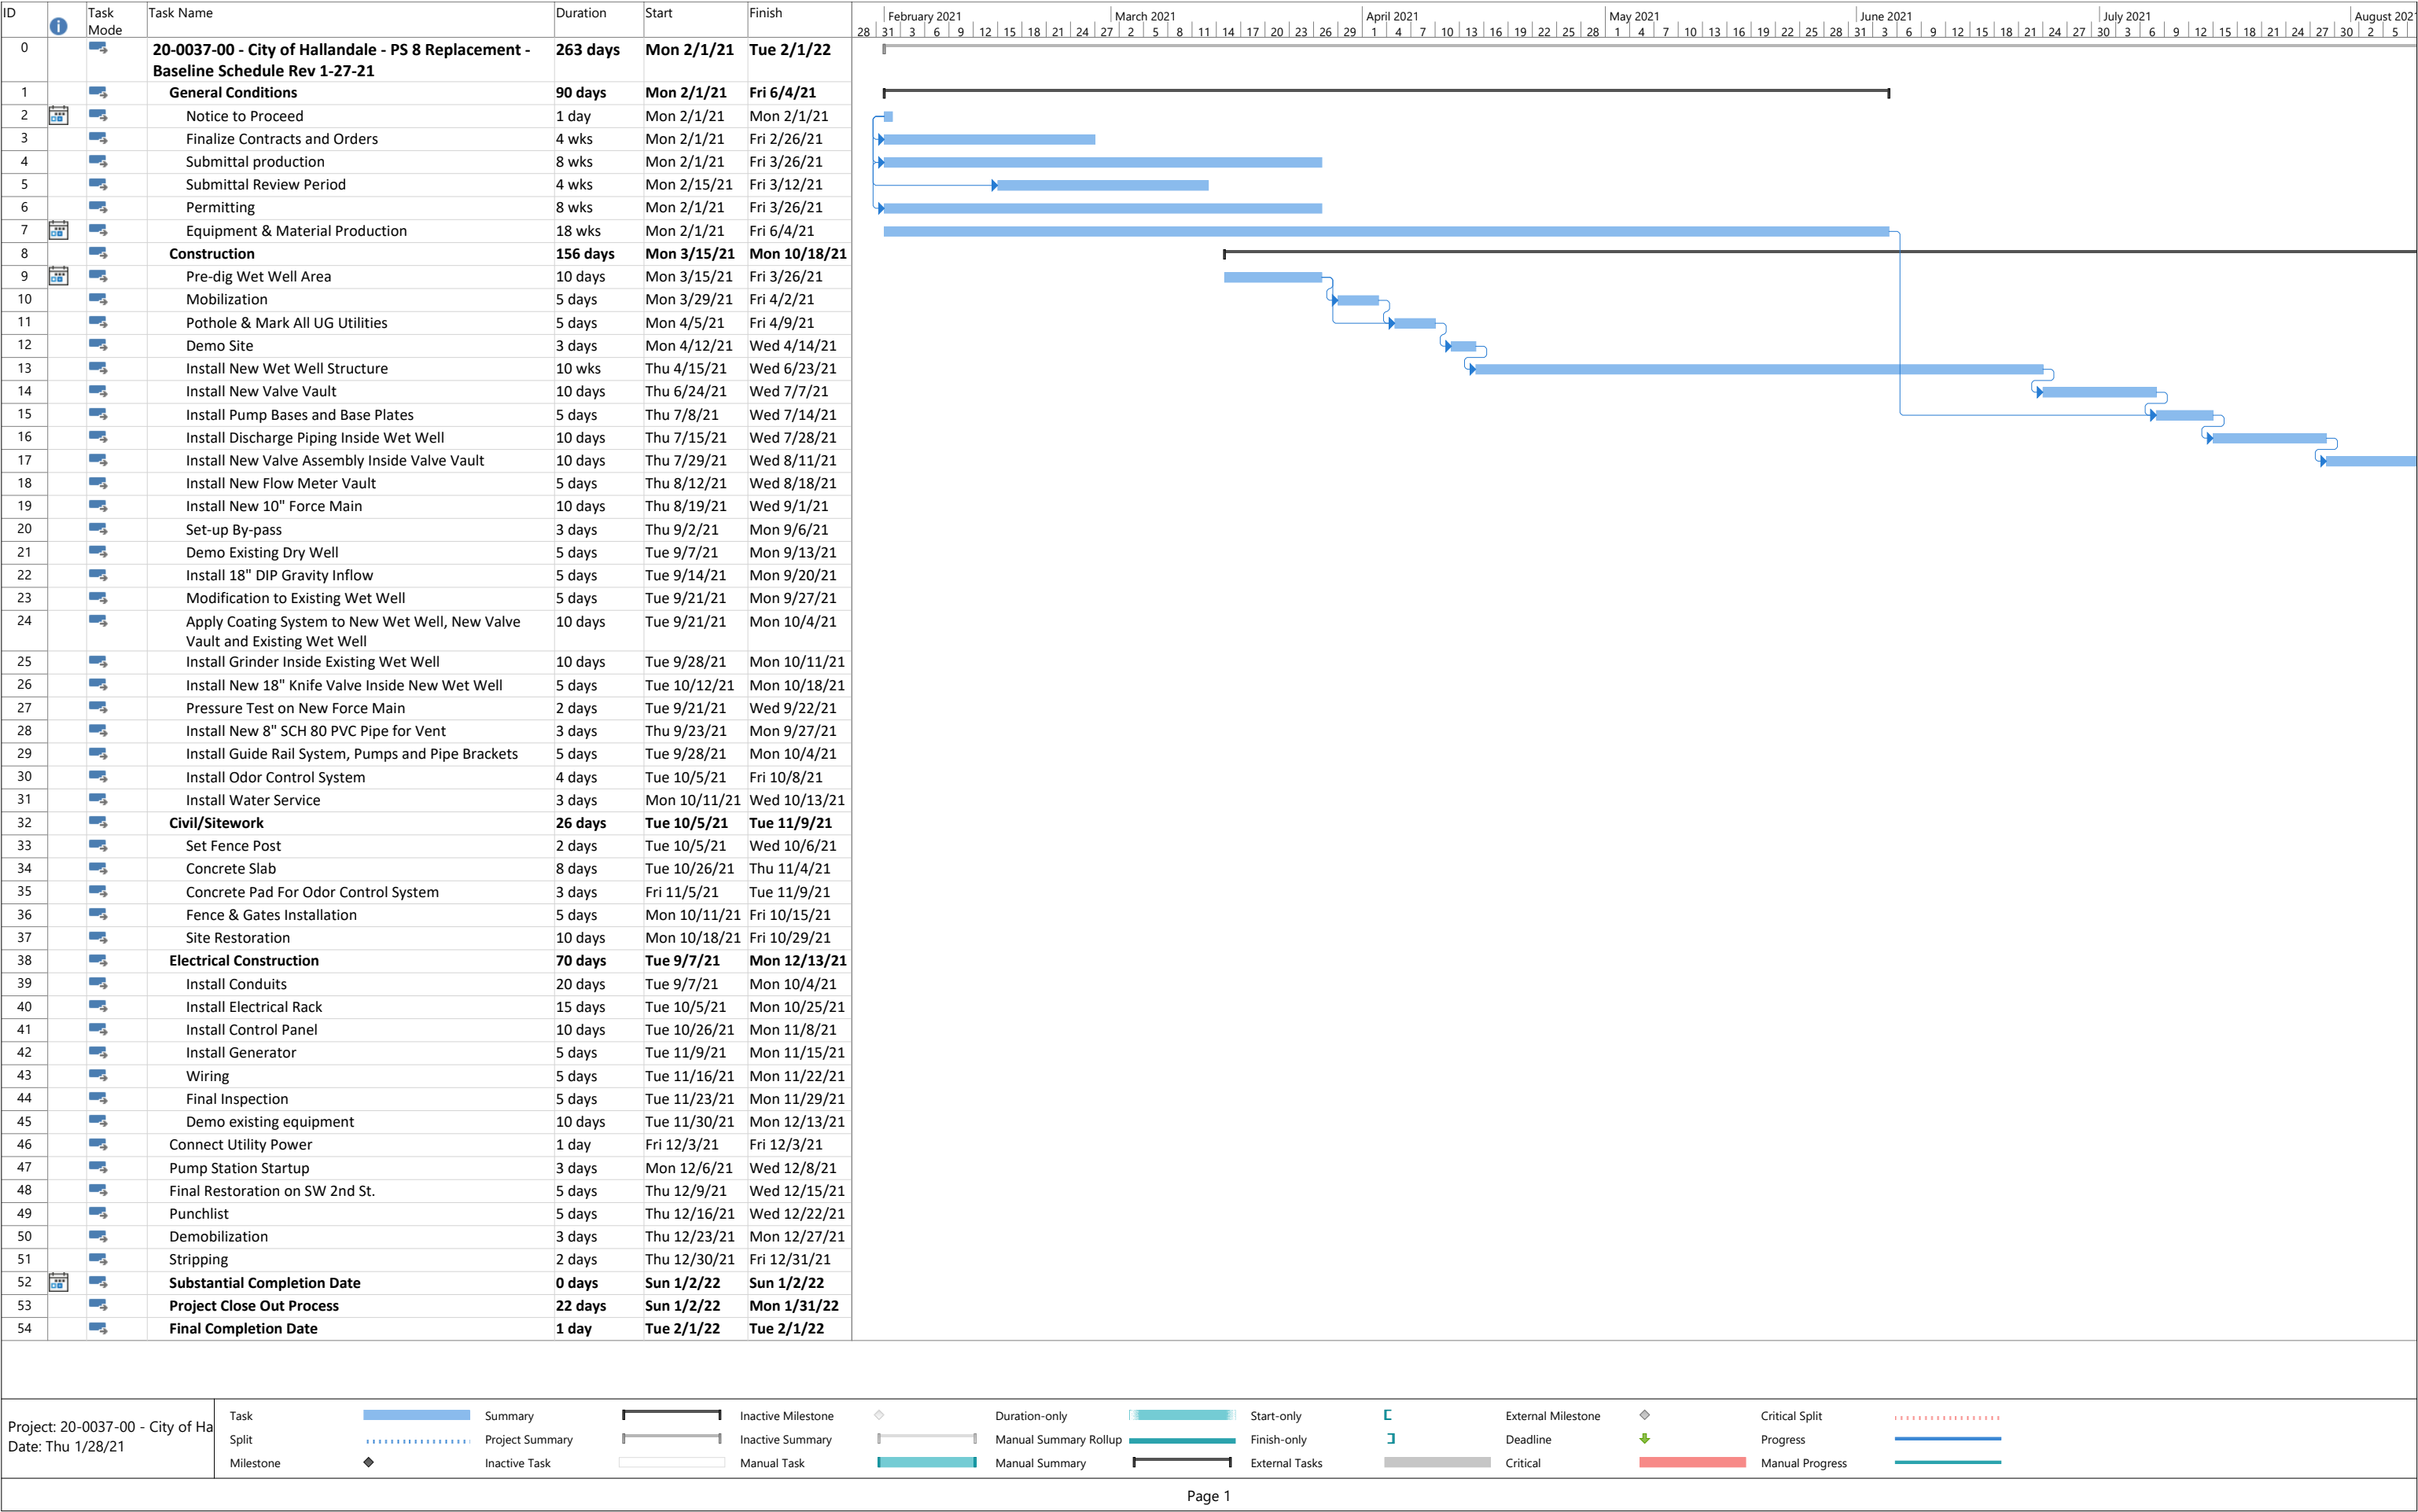

ID	Task Mode	Task Name	Duration	Start	Finish	September 2021							October 2021							November 2021							December 2021							January 2022							February 2022																													
						21	8	11	14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30	3	6	9	12	15	18	21	24	27	30	2	5	8	11	14	17	20	23	26	29	1	4	7	10	13
0		20-0037-00 - City of Hallandale - PS 8 Replacement - Baseline Schedule Rev 1-27-21	263 days	Mon 2/1/21	Tue 2/1/22																																																																	
1		General Conditions	90 days	Mon 2/1/21	Fri 6/4/21																																																																	
2		Notice to Proceed	1 day	Mon 2/1/21	Mon 2/1/21																																																																	
3		Finalize Contracts and Orders	4 wks	Mon 2/1/21	Fri 2/26/21																																																																	
4		Submittal production	8 wks	Mon 2/1/21	Fri 3/26/21																																																																	
5		Submittal Review Period	4 wks	Mon 2/15/21	Fri 3/12/21																																																																	
6		Permitting	8 wks	Mon 2/1/21	Fri 3/26/21																																																																	
7		Equipment & Material Production	18 wks	Mon 2/1/21	Fri 6/4/21																																																																	
8		Construction	156 days	Mon 3/15/21	Mon 10/18/21																																																																	
9		Pre-dig Wet Well Area	10 days	Mon 3/15/21	Fri 3/26/21																																																																	
10		Mobilization	5 days	Mon 3/29/21	Fri 4/2/21																																																																	
11		Pothole & Mark All UG Utilities	5 days	Mon 4/5/21	Fri 4/9/21																																																																	
12		Demo Site	3 days	Mon 4/12/21	Wed 4/14/21																																																																	
13		Install New Wet Well Structure	10 wks	Thu 4/15/21	Wed 6/23/21																																																																	
14		Install New Valve Vault	10 days	Thu 6/24/21	Wed 7/7/21																																																																	
15		Install Pump Bases and Base Plates	5 days	Thu 7/8/21	Wed 7/14/21																																																																	
16		Install Discharge Piping Inside Wet Well	10 days	Thu 7/15/21	Wed 7/28/21																																																																	
17		Install New Valve Assembly Inside Valve Vault	10 days	Thu 7/29/21	Wed 8/11/21																																																																	
18		Install New Flow Meter Vault	5 days	Thu 8/12/21	Wed 8/18/21																																																																	
19		Install New 10" Force Main	10 days	Thu 8/19/21	Wed 9/1/21																																																																	
20		Set-up By-pass	3 days	Thu 9/2/21	Mon 9/6/21																																																																	
21		Demo Existing Dry Well	5 days	Tue 9/7/21	Mon 9/13/21																																																																	
22		Install 18" DIP Gravity Inflow	5 days	Tue 9/14/21	Mon 9/20/21																																																																	
23		Modification to Existing Wet Well	5 days	Tue 9/21/21	Mon 9/27/21																																																																	
24		Apply Coating System to New Wet Well, New Valve Vault and Existing Wet Well	10 days	Tue 9/21/21	Mon 10/4/21																																																																	
25		Install Grinder Inside Existing Wet Well	10 days	Tue 9/28/21	Mon 10/11/21																																																																	
26		Install New 18" Knife Valve Inside New Wet Well	5 days	Tue 10/12/21	Mon 10/18/21																																																																	
27		Pressure Test on New Force Main	2 days	Tue 9/21/21	Wed 9/22/21																																																																	
28		Install New 8" SCH 80 PVC Pipe for Vent	3 days	Thu 9/23/21	Mon 9/27/21																																																																	
29		Install Guide Rail System, Pumps and Pipe Brackets	5 days	Tue 9/28/21	Mon 10/4/21																																																																	
30		Install Odor Control System	4 days	Tue 10/5/21	Fri 10/8/21																																																																	
31		Install Water Service	3 days	Mon 10/11/21	Wed 10/13/21																																																																	
32		Civil/Sitework	26 days	Tue 10/5/21	Tue 11/9/21																																																																	
33		Set Fence Post	2 days	Tue 10/5/21	Wed 10/6/21																																																																	
34		Concrete Slab	8 days	Tue 10/26/21	Thu 11/4/21																																																																	
35		Concrete Pad For Odor Control System	3 days	Fri 11/5/21	Tue 11/9/21																																																																	
36		Fence & Gates Installation	5 days	Mon 10/11/21	Fri 10/15/21																																																																	
37		Site Restoration	10 days	Mon 10/18/21	Fri 10/29/21																																																																	
38		Electrical Construction	70 days	Tue 9/7/21	Mon 12/13/21																																																																	
39		Install Conduits	20 days	Tue 9/7/21	Mon 10/4/21																																																																	
40		Install Electrical Rack	15 days	Tue 10/5/21	Mon 10/25/21																																																																	
41		Install Control Panel	10 days	Tue 10/26/21	Mon 11/8/21																																																																	
42		Install Generator	5 days	Tue 11/9/21	Mon 11/15/21																																																																	
43		Wiring	5 days	Tue 11/16/21	Mon 11/22/21																																																																	
44		Final Inspection	5 days	Tue 11/23/21	Mon 11/29/21																																																																	
45		Demo existing equipment	10 days	Tue 11/30/21	Mon 12/13/21																																																																	
46		Connect Utility Power	1 day	Fri 12/3/21	Fri 12/3/21																																																																	
47		Pump Station Startup	3 days	Mon 12/6/21	Wed 12/8/21																																																																	
48		Final Restoration on SW 2nd St.	5 days	Thu 12/9/21	Wed 12/15/21																																																																	
49		Punchlist	5 days	Thu 12/16/21	Wed 12/22/21																																																																	
50		Demobilization	3 days	Thu 12/23/21	Mon 12/27/21																																																																	
51		Stripping	2 days	Thu 12/30/21	Fri 12/31/21																																																																	
52		Substantial Completion Date	0 days	Sun 1/2/22	Sun 1/2/22																																																																	
53		Project Close Out Process	22 days	Sun 1/2/22	Mon 1/31/22																																																																	
54		Final Completion Date	1 day	Tue 2/1/22	Tue 2/1/22																																																																	

Project: 20-0037-00 - City of Hallandale
Date: Thu 1/28/21

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress

Page 2
