




PARKS G.O. BOND

HALLANDALE BEACH - 2014

PARKS G.O. BOND Beach


HALLANDALE BEACH - 2014

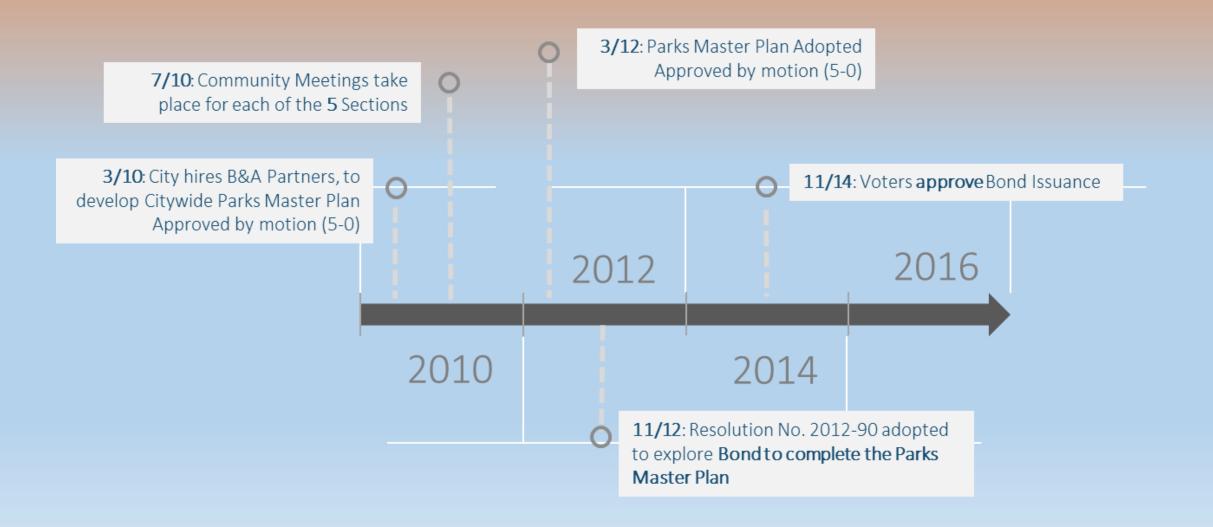

PARKS G.O. BOND Beach

HALLANDALE BEACH - 2014

| | SECTION | PROJECT COSTS B&A \$ (M) | PROJECT COSTS COHB \$ (M) | EST. COMPLETE DATE | STATUS |
|---------------------|---------|--------------------------------|---------------------------------|--------------------|--------------|
| Sunset Park | sw | .02 | .55 | 4/17 | Completed |
| Ingalls Park | SW | .33 | 1.9 | 5/19 | Construction |
| Peter Bluesten Park | SE | 15.2 | 36.5 | 7/19 | Construction |
| GI Tennis Center | SE | .43 | 7.2 | 2/20 | Permitting |
| GI Park | SE | 1.0 | 1.6 | 2/20 | Permitting |
| Historic Village | sw | .03 | .58 | TBD | Development |
| Chaves Lake | NМ | 1.4 | 3.6 | TBD | Development |
| Sunrise Park | NE | .01 | 2.7 | 1/20 | Design |
| Parks Total | | \$18.42 | \$54.6 | | |
| Staffing | | | \$1.7 | | |
| Program Contingency | | | \$1.1 | | |
| Grand Total | | | \$57.4 | | |

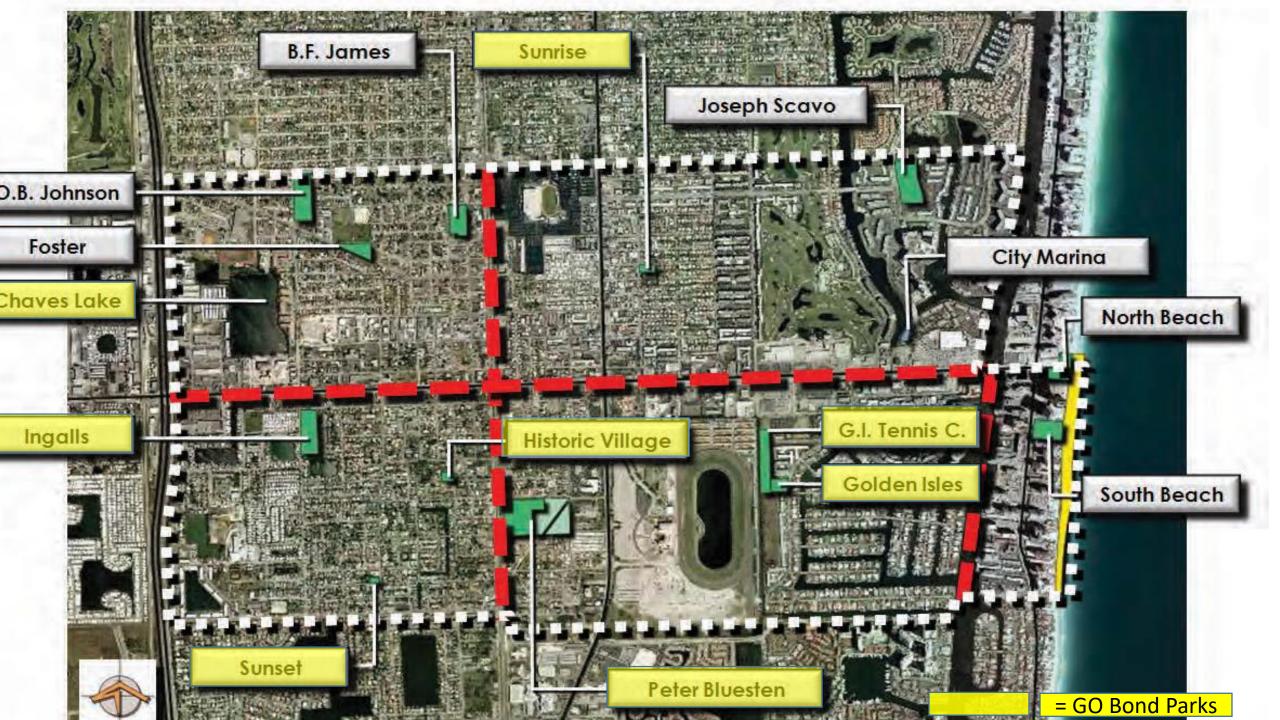







Construction Commencement May 2018











Commencement of Construction Nov 2017

25

PETER BLUESTEN PARK

oogleearth







GOLDEN ISLES TENNIS CENTER AND PARK





GOLDEN ISLES TENNIS CENTER AND GOLDEN ISLES PARK



- Construction drawings have been submitted for permitting
- Commission presentation for GMP approval Feb. 2019
- Estimated Tennis Center and Park closing March 2019
- Estimated Commencement of Construction April 2019









- Two community meetings
- Conceptual design completed
- Commencement of construction TBD







Historic Village



CHAVES LAKE

- Water and soil testing completed
- Survey completed
 - Project currently under review

Parks. For the young and the young at heart





0
